

January 29, 2021

Appleton-Milan Elementary School

Achievements:

- East side roofing, west side duct insulation, gym area roof drains, and west side exterior insulation is complete.
- On the addition exterior, the metal wall panel install is progressing on the west side of the addition, and the west side window installation has started.
- Inside the addition, classroom wall framing, east side duct installation, hydronic piping installation, piping insulation, gym and classroom electrical rough-in is progressing. The underground plumbing rough-in on the east side bathrooms has started.

Next Two Weeks Schedule/Goals:

- East side bathrooms underground plumbing rough-in, gym window glazing and caulking, west side metal wall panels, west side classroom wall framing, gym hydronic piping, and gym electrical rough-in will be completed week of February 1st.
- Work on classroom sink plumbing rough-in, west side window installation, duct installation, hydronic piping installation, and electrical rough-in will continue into the week of February 8th.
- East side exterior wall insulation will start Monday (2/1/21). Concrete work on the east side of the addition, as well as the west side stoops will start Wednesday (2/3/21). The underground plumbing inspection for the east side bathrooms will be Thursday (2/4/21). Gym painting will start Friday (2/5/21). Wall insulation and sheetrock installation will start next week following west side wall framing completion (2/5/21). Finned tube radiation will ship in two weeks, on 2/12/21.
- Building Automation Training has been tentatively scheduled for 2/10/21.



West Side Exterior Wall
Insulation

Mechanical Mezzanine
Concrete



Window Frame Installation

LQPV High School Middle School


Achievements:

- The gym addition hallway floors were prepped (1/27/21) and poured (1/28/21).
- The wood and ag shop mechanical units were preliminarily balanced by the Test and Balance Contractor on Wednesday (1/27/21).
- Metal shop office ceiling tiles reinstalled on Wednesday (1/27/21).

Next Two Weeks Schedule/Goals:

- The gym concrete floors have one more week of curing before lifts can be driven on it. At the end of next week (2/5/21), all concrete should be thoroughly cured so that it can be worked on.
- Starting next week, the metal panel work on the exterior of the gym will be started.
- The new gym window is scheduled to be installed Tuesday (2/9/21), pending completion at Appleton Elementary.

Metal Shop Office Ceiling Tile

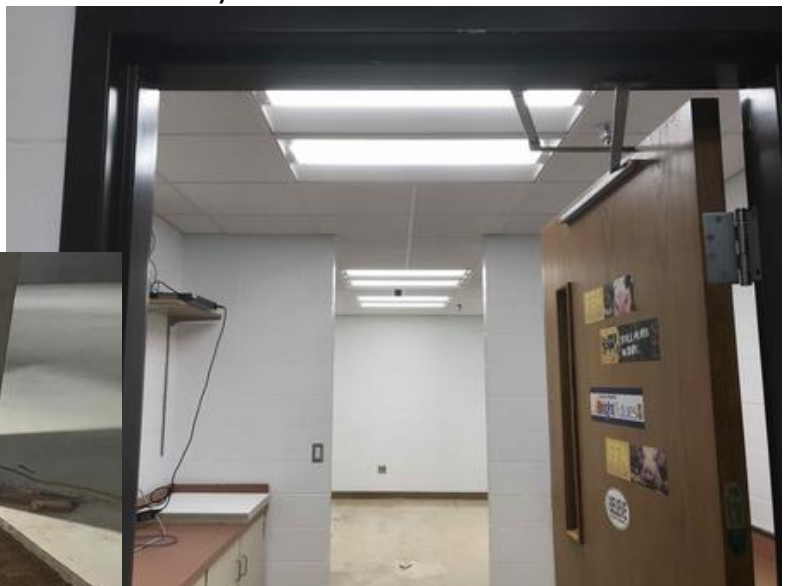

Gym Concrete Prep Work

Madison-Marietta-Nassau Elementary School

Achievements:


- The new gym wood flooring sanding was completed on 1/27/21.
- The sealing process of the new gym wood flooring, and the sanding of the stage wood flooring started 1/27/21.
- The outdoor air dampers on AHU 5 were wired by the controls contractor on 1/27/21.
- Security camera monitor was installed in the main office on 1/27/21.

Near Future Schedule/Goals:

- Front Entrance railing installation tentatively scheduled for Monday, 2/1/21.
- Sanding, sealing, line painting, and finish coating the gym and stage area will continue through the week of February 1 and take approximately three more weeks.



Gym Floor Sealing

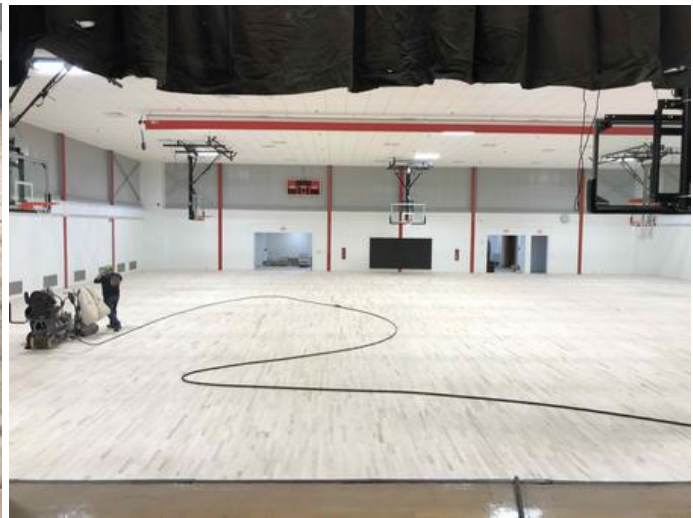

Gym Floor Sanding
