

February 19, 2021

Appleton-Milan Elementary School

Achievements:

- Ceiling painting, electrical rough in and wiring, and seam caulking were completed in the gym.
- On the addition exterior, the east side insulation and wall panel framing is progressing. Windows and doors have been installed up to the finished openings in zone 3.
- Inside the addition, above ground plumbing rough in at classroom sinks, east side and mezzanine duct installation, hydronic piping installation, piping insulation, and classroom electrical rough-in is progressing. The east side concrete work, interior and exterior wall insulation has started. Finned tube radiation was delivered, and installation will start when the gym walls are painted.

Next Two Weeks Schedule/Goals:

- Gym wall painting, mechanical mezzanine exterior wall insulation and sheetrock, and mechanical mezzanine plumbing will start the week of February 22nd.
- Work on east side concrete, sheetrock installation, mechanical mezzanine piping and duct work, classroom sink plumbing rough-in, exterior wall panels, wall insulation, duct installation, hydronic piping installation, and electrical rough-in and wiring will continue into the week of March 1st.
- Mechanical Mezzanine duct drops will be installed the week of February 22nd. Electrical work on the roof will start the week of February 22nd. Piping drops to classroom finned tube radiation will start the week of February 22nd and follow framing of pipe chases.



East Half Concrete

Sheetrock and Exterior
Insulation Install



Window Install

LQPV High School Middle School

Achievements:

- The commons flooring base was installed on 2/17/21.

Next Two Weeks Schedule/Goals:

- The metal panel work on the exterior of the gym was pushed to the week of February 22nd due to cold weather and work in Appleton.
- The new gym window installation will start on Tuesday 2/23/21 following the metal panel installation.
- The new pool locker room AHU will have test and balancing on Wednesday, 2/24/21.
- Due to the cold weather, frost has built up on the exterior walls and footings. The state inspector is requesting that pouring concrete in this area waits until the frost is gone.



Commons Floor Base Install

Commons Floor Base Install



Madison-Marietta-Nassau Elementary School


Achievements:

- Gym Equipment controls were installed and MMN staff was trained on 2/17/21.
- Ceiling tile work was finished in kindergarten restrooms and front lobby area.
- Door Frames were installed in the new gym openings.

Near Future Schedule/Goals:

- Working on punch list items.

Door Frame Install

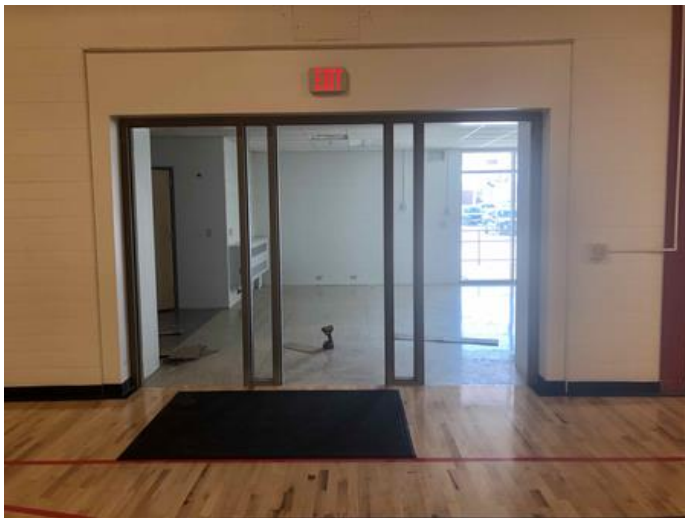

Ceiling Tile Install

