

March 26, 2021

Appleton-Milan Elementary School

Achievements:

- Work from each of the following specialties was performed this week: Plumbing, Electrical, Hydronic Piping and Insulation, HVAC and Insulation, Wall Framing and Insulation, Drywall Hanging and Finishing, Painting, Ext Wall Insulation and Metal Panel Installation, Access Control, Ceiling Grid and Tile, and Window and Door Installation.
- Acoustical wall panels were hung in the Gym.
- A soffit on the exterior of the original building has been identified for removal this week. This will open up a clear, clean transition for all of the water piping (hydronic, domestic, and sprinkler) from the original building to the addition.

Next Two Weeks Schedule/Goals:

- The Gym will be temporarily cleaned out so that Gym equipment (basketball hoops, curtain) can be installed the week of March 29th.
- The remaining store front doors can be installed once the exterior concrete stoops are poured (waiting for the ground to dry), and the exterior metal soffit panels are installed (expected to be delivered this week).
- Interior walls and room finishes are progressing nicely from West to East.
 - Framing on the East end and as a whole is nearing completion.
 - Drywall finishes and ceiling grid installations are complete on the West end and moving East.
 - Electrical finishes and lighting, Fin-tube radiation, HVAC finishes have begun
 - Cabinetry has been delivered and installation will begin in the next two weeks.
 - Flooring, ceiling tile and window finishes will begin in the next month.
- Playground equipment is expected to be delivered the week of April 5th.



Gym Acoustical Panels

Soffit slated for removal



Main East – West Hallway


LQPV High School Middle School

Achievements:

- Electrical rough in the Gym and storage areas was completed this week.
- Duct installation in the storage areas is nearing completion.

Next Two Weeks Schedule/Goals:

- Gym equipment installation will start on April 5th.
- Ceiling paint will has begun and will complete in time for the equipment installation.
- Wall painting will begin shortly after.

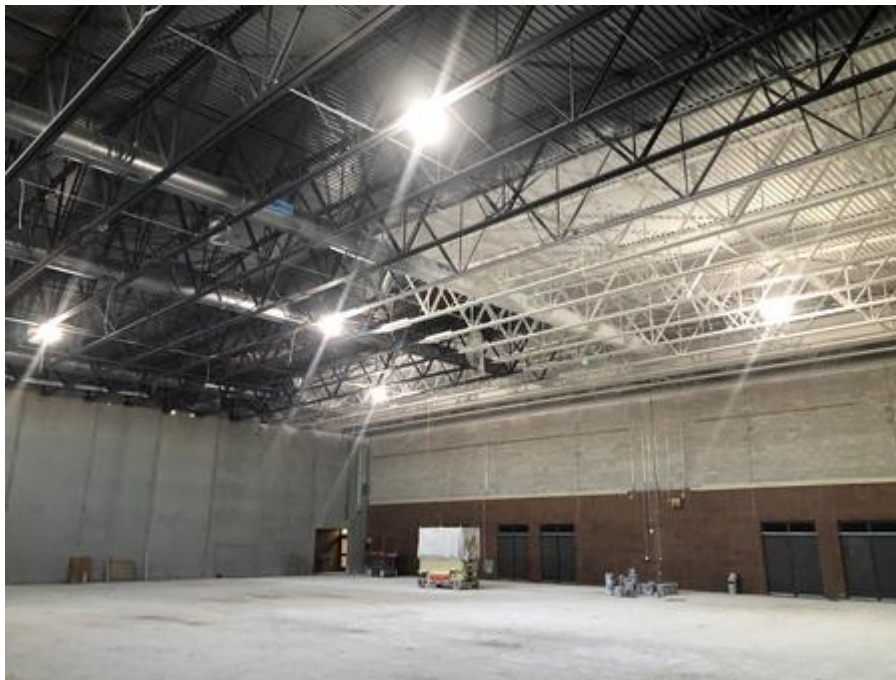

Gym Addition Progress

Madison-Marietta-Nassau Elementary School

Achievements:

- Continued preparation for summer work.

Near Future Schedule/Goals:

- Working on punch list items.
- Chiller startup is tentatively scheduled for a day with warm weather.
