

April 02, 2021

Appleton-Milan Elementary School

Achievements:

- Work from each of the following specialties was performed this week: Plumbing, Electrical, Hydronic Piping and Insulation, HVAC and Insulation, Wall Framing and Insulation, Drywall Hanging and Finishing, Painting, Ext Wall Insulation and Metal Panel Installation, and Selective Demolition.
- Existing exterior soffit was removed to make a clean transition for various water pipes between the original and new buildings.

Next Two Weeks Schedule/Goals:

- Gym equipment (basketball hoops, curtain) was delivered, but installation was delayed one week due to a late delivery caused by vehicle breakdown. Installation will now occur on the week of Apr 5th.
- The remaining store front doors can be installed once the exterior concrete stoops are poured (Friday if weather holds), and the exterior metal soffit panels are installed (delivery expected on Friday).
- Interior walls and room finishes are progressing nicely from West to East.
 - Framing on the East end, and as a whole, is nearing completion.
 - Drywall finishes and ceiling grid installations are complete on the West end and moving East.
 - Electrical finishes and lighting, Fin-tube radiation, HVAC finishes have begun
 - Cabinetry installation will begin next week.
 - Carpet, epoxy coatings and ceramic tile will begin the week of Apr 19th.
 - Ceiling tile and window finishes will begin in the next month.
- Playground equipment is expected to be delivered the week of April 5th.



Gym Equipment

Removed Soffit



Main East – West Hallway


LQPV High School Middle School

Achievements:

- Various trades rough-in work is complete.
- Masonry work is nearing completion.

Next Two Weeks Schedule/Goals:

- Gym equipment (Basketball hoops, volleyball standards, curtains, etc.) installation was pushed back one week due to delivery issues and will start on April 12th.
- Ceiling paint will have begun and will complete in time for the equipment installation.
- Wall painting will begin shortly after.

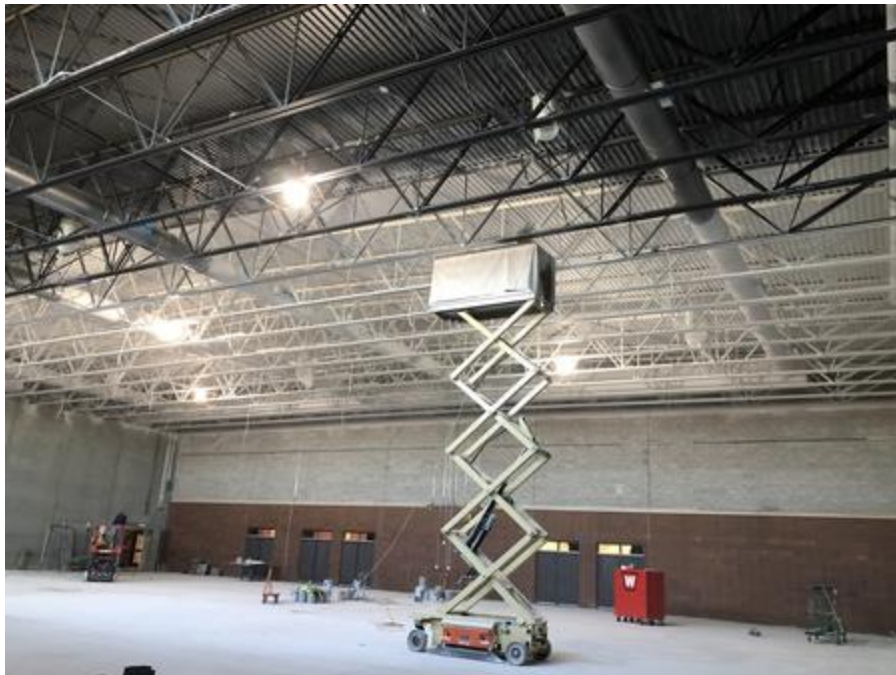

Gym Addition Progress

Madison-Marietta-Nassau Elementary School

Achievements:

- Continued preparation for summer work.
- Blind installation began this week.

Near Future Schedule/Goals:

- Working on punch list items.
- Chiller startup is scheduled for Tuesday, Apr 6th.



Classroom Blinds
