

**April 23, 2021**

## Appleton-Milan Elementary School

### Achievements:

- Work from each of the following specialties was performed this week: Plumbing, Electrical, Hydronic Piping and Insulation, HVAC and Insulation, Wall Framing and Insulation, Drywall Hanging and Finishing, Ceiling Grid and Tile Installation, Painting, Ext Wall Insulation and Metal Panels, Storefront Windows and Doors, Carpet and LVT, Epoxy Floor and Casework Installations.
- Three of five remaining exterior storefront openings were installed.
- Epoxy floors were poured in the West side Boys and Girls bathrooms.
- Carpet and Luxury Vinyl Tile (LVT) has been laid in the West side classrooms.

### Next Two Weeks Schedule/Goals:

- Interior walls and room finishes are progressing nicely from West to East.
  - Rough-ins on the East end, and as a whole, are nearing completion.
  - Drywall finishes and ceiling grid installations are complete on the West end and moving East.
  - Ceiling tile and flooring is installed as rooms are made ready.
  - Electrical finishes and lighting, Fin-tube radiation, HVAC finishes.
  - Casework installations are progressing on the West end.
    - Countertop installations can occur once the sinks have arrived (no firm date).
  - Window finishes will begin in the next month.
- Security, camera and clock installations.
- Ceramic tile installations will begin on Wed 28 Apr.



Epoxy Floor



Mech Room Piping



Carpet & LVT


## LQPV High School Middle School

### Achievements:


- Overflow Roof Drain installations are progressing in the Event Gym.

### Next Two Weeks Schedule/Goals:

- Wall painting is ongoing.

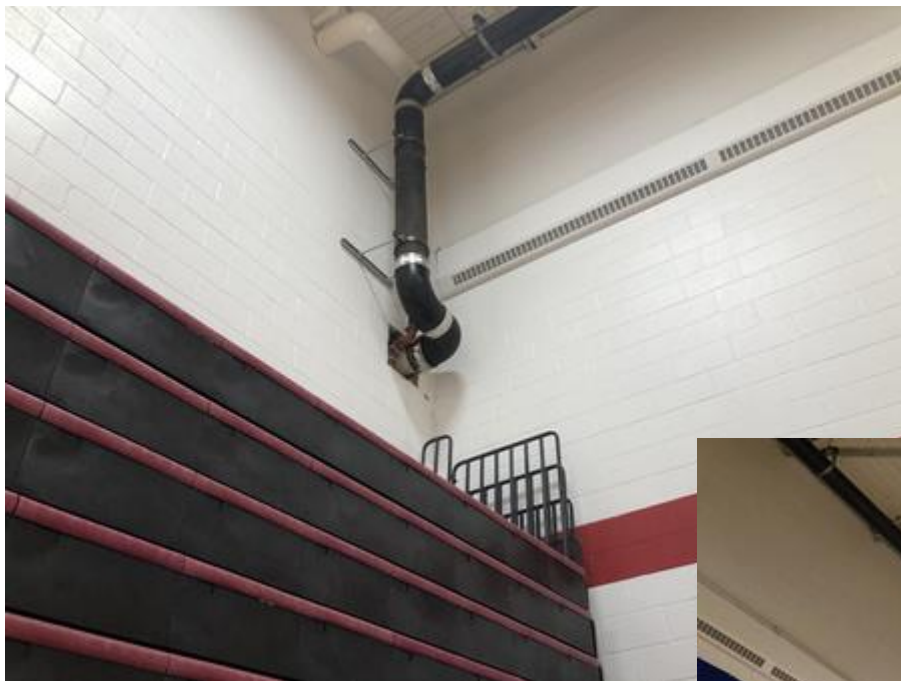

Overflow Roof Drains

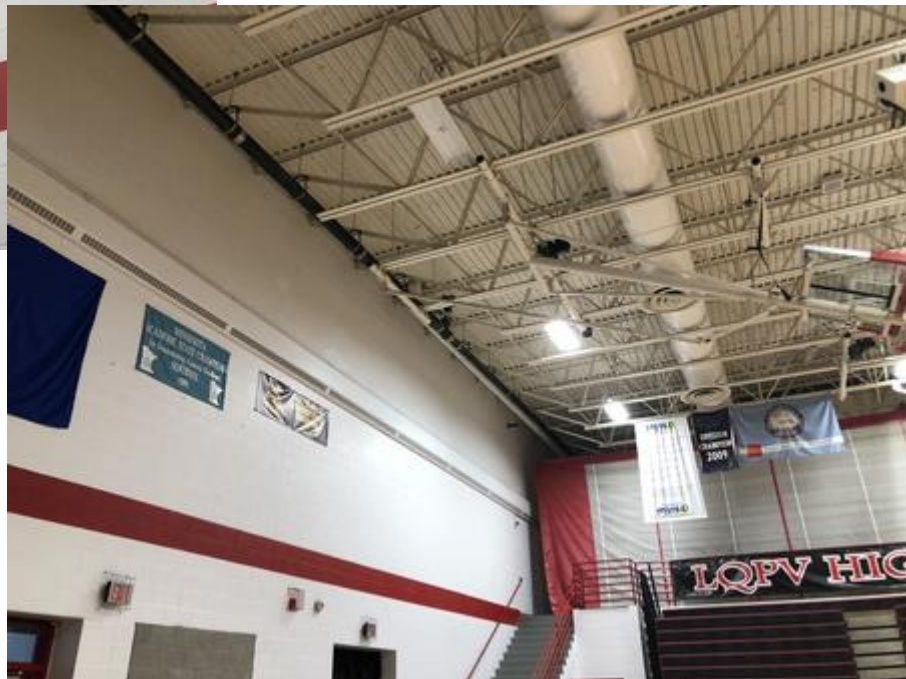

# Madison-Marietta-Nassau Elementary School

### Achievements:

- Continued preparation for summer work.

### Near Future Schedule/Goals:

- Working on punch list items.
