

May 7, 2021


# Appleton-Milan Elementary School

### Achievements:

- Work from each of the following specialties was performed this week: Plumbing, Electrical, Hydronic Piping and Insulation, HVAC and Insulation, Controls, Drywall / Dura-rock Hanging and Finishing, Painting, Ceiling Grid and Tile, Carpet / LVT, Casework and Ceramic Tile Installations.
- West-side classrooms are advanced enough that school soon will begin to unload storage containers directly into the classroom.

### Next Two Weeks Schedule/Goals:

- Interior walls and room finishes are progressing nicely from West to East.
  - Drywall finishes and ceiling grid installations are complete on the West end and moving East.
  - Ceiling tile and flooring is installed as rooms are made ready.
  - Electrical finishes and lighting, Fin-tube radiation, HVAC finishes.
- Security, camera, and clock installations.
- Locker installations are scheduled for the week of 24 May.
- Sinks are being installed with the counter-tops, however the faucets have not arrived. They are expected next week.

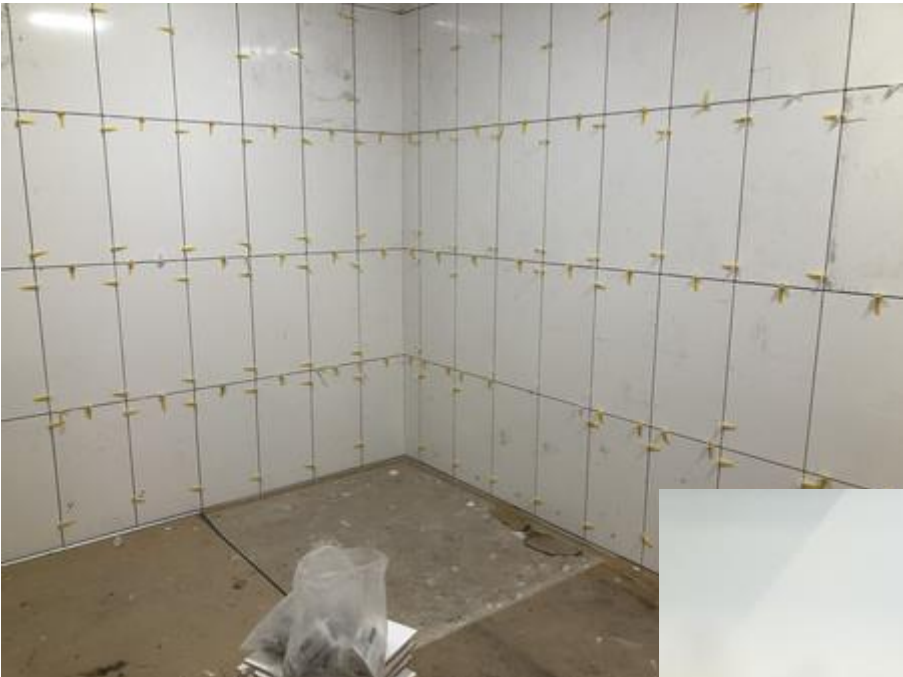

Ceramic Tile



Countertop with Sink



Exterior Entryway

## LQPV High School Middle School

### Achievements:

- Overflow Roof Drain insulation installations are complete.
- Water line for the field sprinkler was laid.

### Next Two Weeks Schedule/Goals:

- Wall painting is ongoing.
- Wall chase drywall and finishing is ongoing.

### Damage Incidents:

- An in-wall sprinkler line was damaged on April 20 and the Event Gym floor was partially flooded the night of April 22. Both incidents were likely caused by the same contractor.
  - April 26: The contractor's insurance company was onsite and both incidents were filed under the same claim.
  - May 5: The flooring company (JWood) who refinished the floor (summer 2020) was onsite to do a damage assessment. A cost estimate outlining recommended action is expected in the near future.



Drywall Chase Installation



Water Line

# Madison-Marietta-Nassau Elementary School

### Achievements:

- A planning / Q&A meeting was held with school / daycare staff to discuss the schedule and needed action items for this summer's daycare renovation.

### Near Future Schedule/Goals:

- Preparation for summer work.
